



TODAY'S DATE  
Wednesday 11th July, 2018  
ROOM CATEGORY  
Deluxe Block  
RENOVATION DATES  
4th June - 12th August

45% COMPLETED - ON SCHEDULE

### Completed work to-date:



- ✓ Removed all tubs and retiled all bathrooms and showers
- ✓ Removal of skirting boards and reinstallation of new skirting boards
- ✓ Created 12 rooms with Patios
- ✓ Removed and enclosed all patio louvres in all 18 rooms
- ✓ Building of roof over ground floor patios and installation of privacy screens between patios

- ✓ Building of privacy screens in the corridors
- ✓ Cleaning Out all bedroom floor tiles and re-grouting
- ✓ Repainting of rooms and painting each room with an accent wall in blue
- ✓ End Suites windows enclosed and re-plastered




### Outstanding work which is in progress:



- ... Removing all sliding doors and installing two 6 panel French doors for the patio.
- ... Build a new roof over 2nd floor staircase
- ... Removal and replacement of Handrail over 2nd staircase
- ... Painting of Roof, Handrails and Panels with privacy screens in the corridors
- ... Installing new room lights

### Outstanding work to be completed:

- ... Installing shower heads in the showers
- ... Installing vanity sinks
- ... Re-installing toilets
- ... Installing bathroom hardware – towel racks, grab bars/shower curtain rods

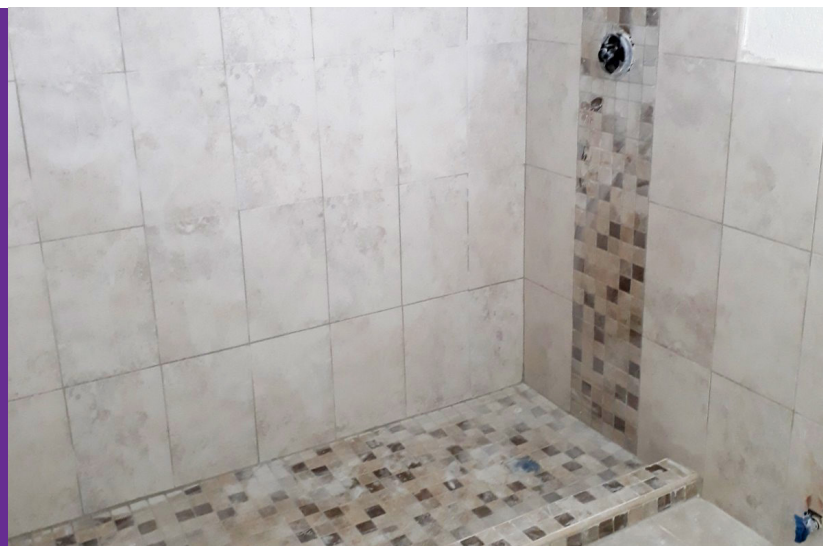

- ... Installing new sheer material for the patio doors
- ... Installing new black out curtains
- ... Outfitting the room with new furniture [which are all on island]
- ... Installing new entrance doors with electronic locks

FOLLOW US ON SOCIAL MEDIA: @timeoutbarbados!
