



TODAY'S DATE
Wednesday 25th July, 2018
ROOM CATEGORY
Deluxe Block
RENOVATION DATES
4th July - 12th August, 2018

75% COMPLETED - ON SCHEDULE

Completed work to-date:



- ✓ Removed all tubs and retiled all bathrooms and showers
- ✓ Removed old skirting boards and reinstalled new skirting boards
- ✓ Created 12 rooms with Patios
- ✓ Removed and enclosed all patio louver windows in all rooms
- ✓ Built a roof over ground floor patios and installed privacy screens between patios on ground floor


- ✓ Built and painted privacy screens in the corridors of the 2nd and 3rd floor
- ✓ Cleaned out all bedroom floor tiles and re-grouted them.
- ✓ Repainted all rooms and added an accent wall in blue
- ✓ End Suites windows enclosed and re-plastered
- ✓ Removed all sliding doors and installed two French doors for the patios




- ✓ Built and painted a new roof over 2nd floor staircase
- ✓ Rebuilt and repainted the handrail for the 2nd floor staircase
- ✓ Installed new heavy duty entrance doors with electronic locks
- ✓ Installed new shower heads in the new showers
- ✓ Re-installed all toilets
- ✓ Built a garden planter in front of each ground floor patio

Outstanding work which is in progress:

- ... Installing new room lights
- ... Installing vanity sinks
- ... Installing new side table lamps
- ... Installing new plants for the garden

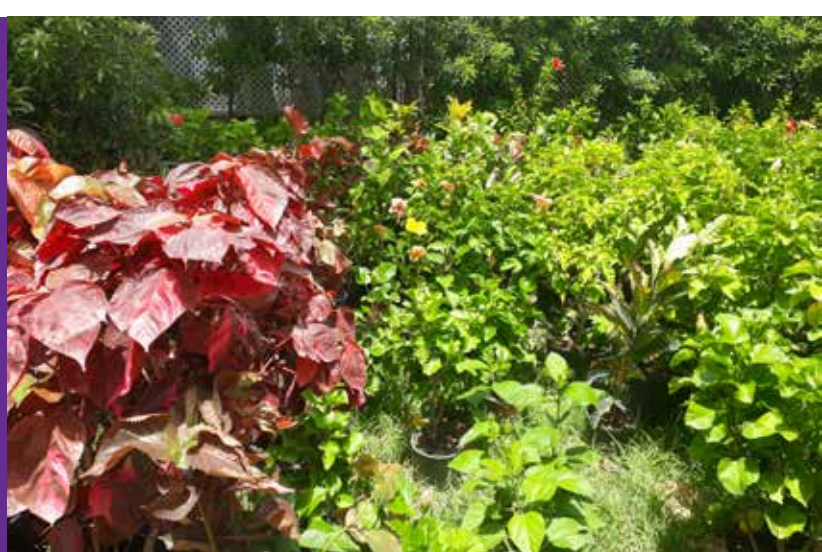

Outstanding work to be completed:

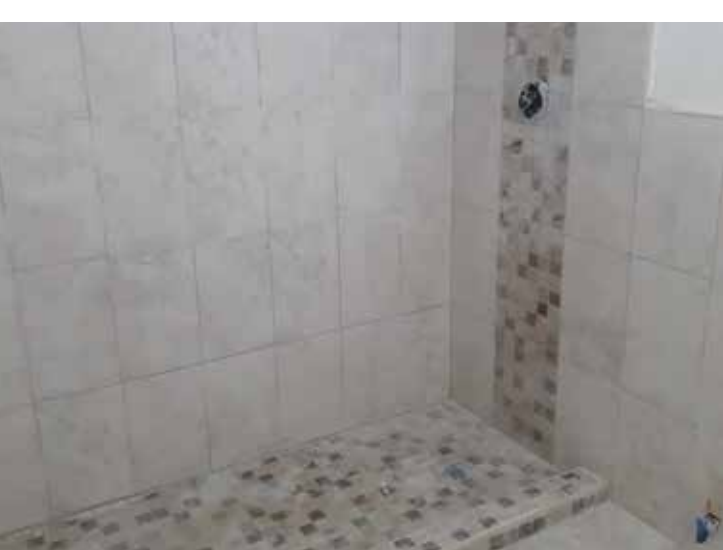

- ... Installing bathroom hardware – towel racks, grab bars/shower curtain rods
- ... Installing new bathroom mirrors
- ... Installing new sheer material for the patio doors
- ... Installing new black out curtains
- ... Outfitting the room with new furniture [which are all on island]

FOLLOW US ON SOCIAL MEDIA: @timeoutbarbados
