



**TODAY'S DATE**  
Tuesday 9th October, 2018  
**ROOM CATEGORY**  
Standard Studio Block  
**COMPLETION DATE (ESTIMATED)**  
17th October, 2018

75% COMPLETED

### Completed work to-date:




- ✓ Removed 8 sliding doors and installed two 6 panel French doors to create small patio
- ✓ Removed all bathroom tubs
- ✓ Removed all vanities
- ✓ Removed all skirting boards and reinstalled new skirting boards
- ✓ Removed all bathroom window louvers and replaced with a modern sash window, with screen protection and security bars.

- ✓ Cleaned Out all bedroom floor tiles and re-grouted the tiles
- ✓ Repainted all rooms and added an accent wall in blue
- ✓ Installed new entry doors with new electronic locks for all 24 rooms
- ✓ Installed new bathroom lights in all 24 rooms



### Outstanding work which is in progress:

- ... Retiling all showers and bathrooms
- ... Installing shower heads in the showers
- ... Installing vanity sinks
- ... Re-installing toilets
- ... Installing bathroom hardware - towel racks, garb bars /shower curtain rods
- ... Re-installing curtains
- ... Installing new sheer material for the window/patio door
- ... Outfitting the room with new furniture - bedheads, side tables, chest of drawers and writing desks

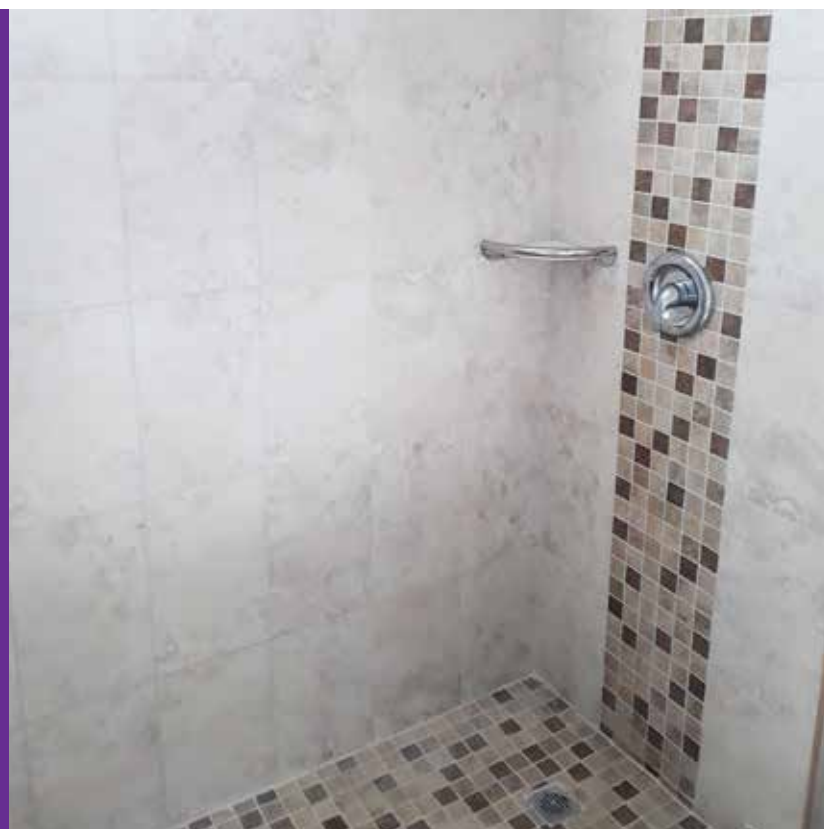

### Update for Phase 3: Pool and Superior Rooms

We wish to inform you that the complete renovations to these 34 rooms are not going to be possible before the start of December 2018. Therefore, we have made the decision to do everything with exception of the bathroom renovations. We will advise the 2019 schedule for the bathrooms soonest. Please note the following that will be done before the upcoming Winter Season:

- ... Outfitting the room with new furniture - bedheads, side tables, chest of drawers and writing desks
- ... Changing the entrance doors with new doors and electronic locks
- ... Painting the rooms
- ... Installing new bedroom curtains and also adding sheer curtains as well

FOLLOW US ON SOCIAL MEDIA: @timeoutbarbados
