




TODAY'S DATE:
 Friday, 30th August 2019
RENOVATION DATES:
 15th August - 17th November 2019
PROGRESS:
 5% completed – on schedule

BATHROOM RENOVATIONS COMPLETED WORK TO-DATE:



- ✓ Removed 7 out of 14 tubs from the Superior Rooms.
- ✓ Removed tiles from 7 out of 20 Pool View Bathrooms.
- ✓ Tiled 14 bathroom floors.

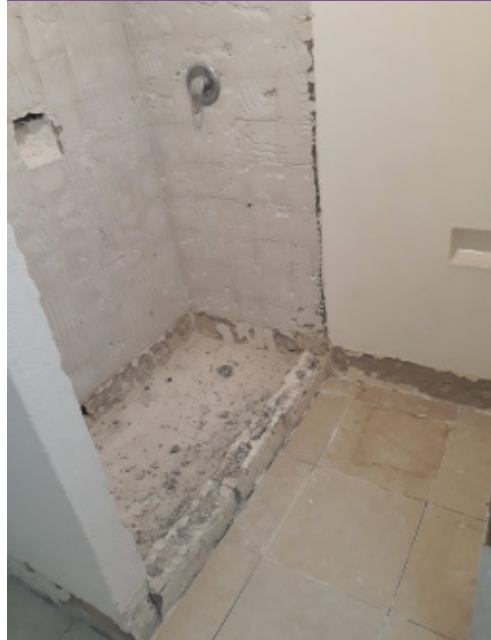

OUTSTANDING WORK TO COMMENCE:

- Construction of our new Gym
- Construction of our new Front Desk
- Construction of our Pool Deck extension.
- Re-paving our Car Park.
- Installing our Solar Water Heaters for our Standard, Superior and Pool View Rooms.
- Installing our Generator.

NEXT UPDATE: FRIDAY, 13TH SEPTEMBER 2019

FOLLOW US ON   @TIMEOUTBARBADOS
